



कार्यालय अधिशासी अभियन्ता, खण्ड कार्यालय,

उ०प्र० जल निगम (ग्रामीण), सुलतानपुर
विनोवापुरी (लोलेपुर), निकट वर्मा उपवन, सुलतानपुर

E-mail:- exenjn_sultanpur@yahoo.com

पत्रांक
सेवा में,

5635 / 679 / 125
मुख्य अभियन्ता(ग्रामीण),
उ०प्र० जल निगम(ग्रामीण),
लखनऊ।

दिनांक 14/09/2026

विषय:- दैनिक समाचार पत्र डिजिटल मीडिया हिन्दुस्तान में दिनांक 14.09.2026 में प्रकाशित नकारात्मक खबर के संबंध में।

महोदय,

उपरोक्त विषयक डिजिटल मीडिया दैनिक हिन्दुस्तान में प्रकाशित खबर 'निर्माण में पीली ईट लगाने की शिकायत' के संदर्भ में अवगत कराना है कि विकासखण्ड-कूरेभार के अन्तर्गत लोकेपुर पाइप पेयजल योजना का निर्माण कार्य मेसर्स विन्ध्या टेलीलिंक-गाजा जेवी, नोएडा द्वारा करवाया जा रहा है। उक्त प्रकरण संज्ञान में लेकर योजना में प्रयुक्त खराब गुणवत्ता के ईट का प्रयोग तत्काल कार्यस्थल से हटवा दिया गया (फोटोग्राफ संलग्न) है तथा योजना में प्रयुक्त सामग्री का समय-समय पर जाँच करवायी जाती (मटेरियल टेस्टिंग रिपोर्ट संलग्न) है। वर्तमान में योजना पर गुणवत्तायुक्त मटेरियल प्रयुक्त किया जा रहा है जिसकी मॉनिटरिंग थर्ड पार्टी एजेन्सी मेसर्स फिचनर, टी०पी०आई०, सुलतानपुर द्वारा किया जा रहा है।

उक्त योजना में नलकूप-01 नग, पम्पहाउस-01 नग, बाउन्ड्रीवाल-01 नग उच्च जलाशय (175 कि०मी०/16 मी०)-01 नग, सोलर-01 नग, पाइप लाइन-15.94 किमी० तथा गृह जल संयोजन-595 नग प्रस्तावित है। प्रस्तावित कार्यों के सापेक्ष नलकूप-01 नग पूर्ण, पम्पहाउस-01 नग पूर्ण, बाउन्ड्रीवाल-01 नग पूर्ण, उच्च जलाशय-01 नग जिक एलम टैंक अधिष्ठापित (80%) तक पूर्ण, सोलर-01 नग पूर्ण, पाइप लाइन-15.20 किमी० पूर्ण, तथा गृह जल संयोजन-257 नग पूर्ण है शेष कार्य प्रगति पर है।

कार्यदायी फर्म द्वारा अपने पत्रांक VTL-GAJA JV/DWSM/SLNP/2026-27/98 दि० 14.09.2026(संलग्न) द्वारा अवगत कराया गया है वर्तमान में योजना प्रगति पर है जिसे दिनांक 10 अक्टूबर, 2026 तक पूर्ण कराकर जलापूर्ति प्रारम्भ करा दिया जायेगा।

अतः आपसे अनुरोध है कि उक्त प्रकरण को निक्षेपित करवाने की कृपा करें।

संलग्नक:-उपरोक्तानुसार।

भवदीय

(सुभाष चन्द्र)
अधिशासी अभियन्ता

पृ०सं० एवं दिनांक :-उपरोक्तानुसार।

प्रतिलिपि:- निम्नलिखित को सूचनार्थ एवं आवश्यक कार्यवाही हेतु प्रेषित-


1. जिलाधिकारी, सुलतानपुर।
2. मुख्य विकास अधिकारी, सुलतानपुर।
3. मुख्य अभियन्ता(ल०क्षेत्र), उ०प्र० जल निगम(ग्रामीण), लखनऊ।
4. अधीक्षण अभियन्ता, मण्डल कार्यालय, उ०प्र० जल निगम(ग्रामीण), अयोध्या कैम्प-बाराबंकी।
5. अधिशासी अभियन्ता, खण्ड कार्यालय (वि०/या०), उ०प्र० जल निगम (ग्रामीण), अयोध्या।
6. जिला सूचना अधिकारी, सुलतानपुर।
7. श्री प्रमोद कुमार, सहायक अभियन्ता/पी०के० छाबड़ा, जूनियर इंजीनियर।
8. डी०पी०एम०-मेसर्स फिचनर, टी०पी०आई०, सुलतानपुर।
9. प्रोजेक्ट मैनेजर, मे० विन्ध्या टेलीलिंक-गाजा जे०वी०, नोएडा को इस निर्देश के साथ कि योजना के अवशेष कार्यों को शीघ्र पूर्ण कराते हुये नियमित जलापूर्ति प्रारम्भ करवाना सुनिश्चित करें।

अधिशासी अभियन्ता

विकासखण्ड—कूरेभार के अन्तर्गत लोकेपुर पाइप पेयजल योजना पर प्रयुक्त
खराब गुणवत्ता का ईंट हटवाने का फोटोग्राफ



विकासखण्ड-कूरेभार के अन्तर्गत लोकेपुर पाइप पेयजल योजना के कैम्पस का फोटोग्राफ

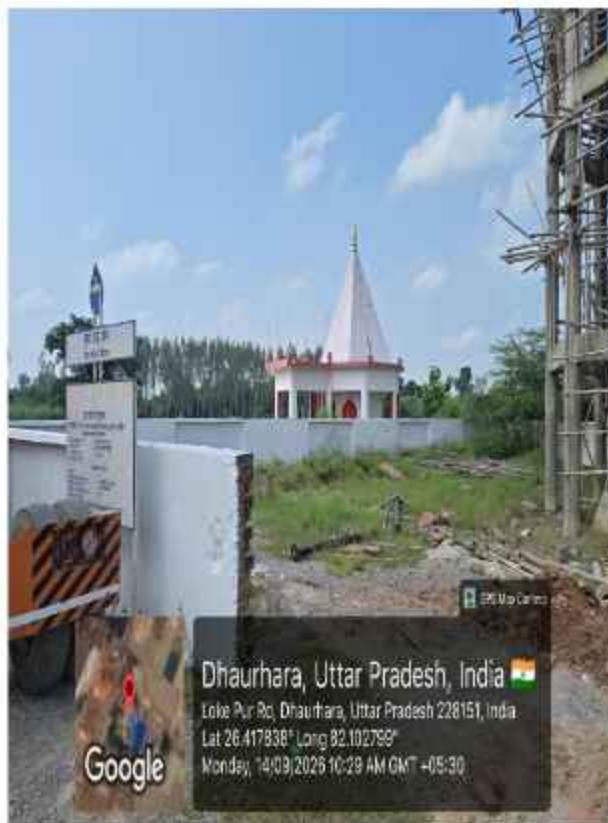



Vindhya Telelinks Limited - Gaja Engineering Private Limited

Brick test (As per 3495)

QUALITY MANAGEMENT SYSTEM

FORMAT No-QA/03



Project : J/M, Sultanpur uttar pradesh

Client : UP Jainigam Sultanpur

Consultant : M/S Fichtner Consulting Engineers Pvt Ltd

Source : Brand Name

SHUBH

Date:- 13/06/26
Block:- Kurebhan
GP name:- Lokepur
No of sample selected:- 05

B/w

(A) DIMENSION CHECK

DIMENSIONS	OBSERVATION	SPECIFIED LIMIT (IS-1077)
Length in (mm)	230	4600+/- 80 mm
Width in (mm)	110	2200+/- 40 mm
Height in (mm)	70	1400+/- 40 mm

(B) WATER ABSORPTION

OBSERVATION	SAMPLE NO					AVG.
Weight after 24 hours soaking (W1) gm	1	2	3	4	5	
	3381	3245	3131	3178	3189	
Dry weight (W2) gm.	2919	2892	2729	2843	2901	
% of water absorption 100 * (W1-W2)/W2 gm.	15.83%	12.21%	14.73%	11.78%	9.93%	12.90%

(C) COMPRESSIVE STRENGTH:-

OBSERVATION	SAMPLE NO					AVG.
Length in (mm)	1	2	3	4	5	
	230	230	230	230	230	
Width in (mm)	110	110	110	110	110	
Height in (mm)	25300	25300	25300	25300	25300	
Load in (N)	289	297	285	299	290	
Compressive strength (N/mm ²)	11.42	11.74	11.26	11.82	11.46	11.54

Signature of site representative

CLIENT/CONSULTANT VHKansh



Vindhya Telelinks Limited - Gaja Engineering Private Limited



SIEVE ANALYSIS (FINE AGGREGATE)
(As Per IS:383)

QUALITY MANAGEMENT
SYSTEM

FORMAT No - QA/04

Project Jai Jeewan Mission Project, Sultanpur (U.P.)

Client U P Jai Nigam Sultanpur

Consultant M/S Fichtner Consulting Engineers Pvt Ltd

Source

LOCATION :

GP- Lokepur

B/w

Date 12/06/20

BLOCK- Kutebhan

Total Weight of Sample (gm) Taken : 1100 gms

Sieve Size	Wt Retained	Cum Wt Retained	Cum % Wt Retained	Cum % Passing	Percentage Passing as Per IS 383			
					Zone 1	Zone 2	Zone 3	Zone 4
10 mm	0.00	0.00	0.00	100.00	100	100	100	100
4.75 mm	49	49	4.45	95.55	90 - 100	90 - 100	90 - 100	95 - 100
2.36 mm	149	198	18.00	82.00	60 - 95	75 - 100	85 - 100	95 - 100
1.18 mm	135	333	30.27	69.73	30 - 70	55 - 90	75 - 100	90 - 100
600 mic	239	572	52.00	48.00	15 - 34	35 - 59	60 - 79	80 - 100
300 mic	257	829	75.36	24.64	5 - 20	8 - 30	12 - 40	15 - 50
150 mic	261	1090	99.09	0.91	0 - 10	0 - 10	0 - 10	0 - 15
Pass	10	1100						

Zone of Fine Aggregate Zone 2 nd

(Fineness Modulus = Sum of Cum % of Wt

Retained / 100) 2.79

Fine Sand- 2.20 Medium Sand- Course Sand-
to 2.60 2.60 to 2.90 2.90 to 3.20

REMARKS

Signature of VTL Representative

CLIENT/CONSULTANT

CHK



Vindhya Telelinks Limited - Gaja Engineering Private Limited

SIEVE ANALYSIS (FINE AGGREGATE)
(As Per IS 383)

QUALITY MANAGEMENT
SYSTEM



Project : Jal Jeevan Mission Project, Sultanpur (U.P.)

Client : U.P. Jal Nigam Sultanpur

Consultant : M/S Fichtner Consulting Engineers Pvt Ltd

Source

LOCATION :

GP- Lokeshpur

P/H

Date 9/06/26

BLOCK- Kurebhan

Total Weight of Sample (gm) Taken : 1100 gms

Sieve Size	Wt. Retained	Cum Wt. Retained	Cum % Wt. Retained	Cum % Passing	Percentage Passing as Per IS 383			
					Zone 1	Zone 2	Zone 3	Zone 4
10 mm	0.00	0.00	0.00	100.00	100	100	100	100
4.75 mm	46	46	4.18	95.82	90 - 100	90 - 100	90 - 100	95 - 100
2.36 mm	151	197	17.91	82.09	60 - 95	75 - 100	85 - 100	95 - 100
1.18 mm	131	328	29.82	70.18	30 - 70	55 - 90	75 - 100	90 - 100
600 mic	241	569	51.73	48.27	15 - 34	35 - 59	60 - 79	80 - 100
300 mic	259	828	75.27	24.73	5 - 20	8 - 30	12 - 40	15 - 50
150 mic	261	1089	99.00	1.00	0 - 10	0 - 10	0 - 10	0 - 15
Pan	11	1100						

Zone of Fine Aggregate: Zone 2 nd

(Fineness Modules = Sum of Cum % of Wt.

Retained / 100) :

2.78

Fine Sand- 2.20 Medium Sand- 2.60 to 2.90 Course Sand- 2.90 to 3.20

REMARKS:

Signature of VTL Representative

CLIENT/CONSULTANT



Vindhya Telelinks Limited - Gaja Engineering Private Limited

Brick test (As per 3495)

QUALITY MANAGEMENT SYSTEM

FORMAT No-QA/03



Project : JIM, Sultanpur uttar pradesh
Client : UP Jainigam Sultanpur
Consultant : M/S Fichtner Consulting Engineers Pvt Ltd

Block:- Kushtimur

GP name:- Lokapur

Date:- 11/06/2016

Source:

Brand Name SHUBH

No of sample selected:- 08

P/H

(A) DIMENSION CHECK

DIMENSIONS	OBSERVATION	SPECIFIED LIMIT (IS-1077)
Length in (mm)	230	4600+/- 80 mm
Width in (mm)	110	2200+/- 40 mm
Height in (mm)	70	1400+/- 40 mm

(B) WATER ABSORPTION

OBSERVATION

SAMPLE NO

	1	2	3	4	5	AVG.
Weight after 24 hours soaking (W1) gm	3298	3197	3031	3121	3339	
Dry weight (W2) gm	2919	2892	2729	2783	2918	
% of water absorption 100*(W1-W2)/W2 gm	12.98%	10.55%	11.07%	12.15%	14.43%	12.23%

(C) COMPRESSIVE STRENGTH:-

SAMPLE NO

OBSERVATION	1	2	3	4	5	AVG.
Length in (mm)	230	230	230	230	230	
width in (mm)	110	110	110	110	110	
Area in (sq mm)	25300	25300	25300	25300	25300	
Load in (KN)	287	301	309	289	308	
Compressive strength (N/mm ²)	11.34	11.90	12.21	11.42	12.17	11.81
Effluorescence						

REMARK :

Signature of VTL Representative

CLIENT/CONSULTANT

Utkarsh



Vindhya Telelinks Limited - Gaja Engineering
Private Limited

SIEVE ANALYSIS (COARSE AGGREGATE)
(As Per IS 383)

QUALITY MANAGEMENT
SYSTEM

FORMAT No - QA/05



Project : JJM, Sultanpur

Date : 25/12/23

Client : UP Jalnigam Sultanpur

Consultant : M/S Fichtner Consulting Engineers Pvt Ltd

Source :

Area of unloading

Block Kurebhar

G.P. JOKEPUR

Total Weight of Sample (gm) Taken :

3000 gms

Max Size of Aggregate (mm)	IS Sieve (mm)	Weight Retained (gm)	Cumm. Weight Retained (gm)	Cumm. % Weight Retained	% Passing	Requirement as per IS 383-2016			
40 mm	63					100			
	40					85-100			
	20					0-20			
	10					0-5			
	Pan					-			
20 mm	40	0.00	0.00	0.00	100.00		100		
	20	330	330	11.00	89.00		85-100		
	10	2514	2844	94.80	5.20		0-20		
	4.75	145	2989	99.63	0.37		0-5		
	Pan	11	3000				-		
10 mm	12.5	0.00	0.00	0.00	100.00				100
	10	360	360	12.00	88.00				85-100
	4.75	2581	2941	98.03	1.97				0-20
	2.36	47	2988	99.60	0.40				0-5
	PAN	12	3000						

Remark:

Failed

Signature of VTL Representative

CLIENT/CONSULTANT



Vindhya Telelinks Limited - Gaja Engineering Private Limited



FORMAT No QA/04

QUALITY MANAGEMENT
SYSTEM

SIEVE ANALYSIS (FINE AGGREGATE)
(As Per IS 383)

Date 25/12/23

Project : Jal Jeevan Mission Project, Sultanpur (U.P.)

Client : U.P. Jal Nigam Sultanpur

BLOCK Kurebhar

Consultant : M/S Fichtner Consulting Engineers Pvt Ltd

LOCATION :

GP. Lokapur

Source :

Total Weight of Sample (gm) Taken : 1000 gm's

Sieve Size	Wt. Retained	Cum Wt. Retained	Cum % Wt Retained	Cum % Passing	Percentage Passing as Per IS 383			
					Zone 1	Zone 2	Zone 3	Zone 4
10 mm	0	0	0	100	100	100	100	100
4.75 mm	87	87	8.70	91.30	90-100	90-100	90-100	95-100
2.36 mm	60	147	14.70	85.30	60-95	75-100	85-100	95-100
1.18 mm	136	283	28.30	71.70	30-70	55-90	75-100	90-100
600 mic	293	576	57.60	42.40	15-34	35-59	60-79	80-100
300 mic	247	817	81.70	18.30	5-20	8-30	12-40	15-50
150 mic	172	989	98.90	1.10	0-10	0-10	0-10	0-15
Pan	11	1000	—	—				

Zone of Fine Aggregate:

(Fineness Modules = Sum of Cum % of Wt. Retained / 100) :

Fine Sand- 2.20 to 2.60 Medium Sand- 2.60 to 2.90 Course Sand- 2.90 to 3.20

REMARKS

Passed.

Signature of Client Representative

Signature of VTL Quality Manager

CLIENT CONSULTANT

Vindhya Telelinks Limited - Gaja Engineering Private Limited JV

Club125, 6th Floor, Tower 'A', Plot No. -3, 4 & S, Sector 12S, Noida-201301, India

Phone: +91-120-4980200 | Fax: +91-120-4980222 | Email: info@vtl-evva.com

PAN: AAHAV1983F | GSTIN: 09AAHAV1983F1Z4

Letter No: VTL-GAJA JV/DWSM/SLNP/2026-2027/98

Date: 14.09.2026

To,
Executive Engineer (Civil)
U.P. Jai Nigam (Rural)
Sultanpur, Uttar Pradesh

Reference: Survey, Design, Preparation of DPR, Construction, Commissioning and O&M for 10 Years of Various Rural Water Supply Projects in the State of Uttar Pradesh as per Request for Proposal for Phase-3 Division- Ayodhya(Sultanpur).

Subject :- Submission of Completion Plan of Lokepur (Block Kurebhar).

Dear Sir,

With Reference to above subject, We are hereby submitting to you updated progress and Completion plan of Lokepur (Block Kurebhar). Total Estimate Cost Rs 328.1 Lakhs.

S.NO	COMPONENTS	SCOPE	COMPLETED	BALANCE	TARGET DAY OF COMPLETION
1	Tubewell (Nos)	1	1	0	
2	OP & Compressor(Nos)	1	1	0	
3	Pump House(Nos)	1	1	0	25-sep-26
4	BW(Nos)	1	1	0	25-sep-26
5	Distribution(Kms)	15940	15200	740	25-Sep-26
6	FHTC(Nos)	595	257		30-Sep-26
7	Solar(Kw)	1		1	30-sep-26
8	Regular Water Supply	595	0	595	10-oct-26
9	OHT(175 KL 16M Staging)-Job	1	0.8	0.2	10-oct-26

Thanking you and assuring you of our best services at all the times.


Your Sincerely,

For Vindhya Telelinks Ltd. - Gaja Engineering Pvt. Ltd. JV
(Authorized signatory)

निर्माण में पीली ईंट लगाने की शिकायत

अव्यवस्था

कूरेभार सुल्तानपुर। ब्लॉक के लोकेपुर गांव में जल जीवन मिशन की हर घर जल योजना के तहत हो रहे निर्माण कार्य की गुणवत्ता पर सवाल उठने लगा है। ग्राम प्रशासक और ग्रामीण इस बात से नाराज हैं। निर्माणाधीन पानी की टंकी के साथ बन रहे कमरे में पीली ईंट और घटिया निर्माण सामग्री के इस्तेमाल का आरोप है।

ग्रामीणों ने आरोप लगाया है कि निर्माण कार्य में मानकों का ध्यान नहीं रखा गया है। उन्होंने इसकी शिकायत बड़े अधिकारियों से की है। रविवार



निर्माण में घटिया किस्म की पीली ईंट के हो रहे निर्माण को दिखाता ग्रामीण।

सुबह ग्राम प्रशासक राधेश्याम वर्मा ने निर्माण स्थल का दौरा किया।

वहां पीली ईंट का इस्तेमाल होते देख उन्होंने नाराजगी जताई। राधेश्याम वर्मा

का कहना है कि जल जीवन मिशन के काम में अच्छी गुणवत्ता की सामग्री का प्रयोग न होने से निर्माण प्रभावित होगा। इससे ग्रामीणों को योजना का लाभ लंबे समय तक मिल पाएगा। बताया गया कि इससे पहले भी इसी योजना के तहत बन रही पानी की टंकी की बाउंड्रीवाल में पीली ईंट लगाने पर ग्रामीणों ने विरोध किया था। अब दोबारा से निर्माणाधीन कमरे में पीली ईंट के इस्तेमाल से यह मामला फिर से चर्चा में आ गया है। ग्रामीणों का कहना है कि अगर सरकारी योजना के निर्माण में क्वालिटी के मानकों को नजरअंदाज किया गया, तो भवन की मजबूती और उपयोगिता पर सवाल उठेंगे।
